

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	01/08/2026
Start of Curtailment (G1 - non Priority)	9:00
End of Curtailment (G1 - non Priority)	16:45
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2766.7 MWh
Total Estimated Curtailed Energy:	1243.8 MWh
Percentage of Curtailed Energy:	44.96%

Scada PVs Generation on 01/08/2026 (curtailment time: 09:00 - 16:45)

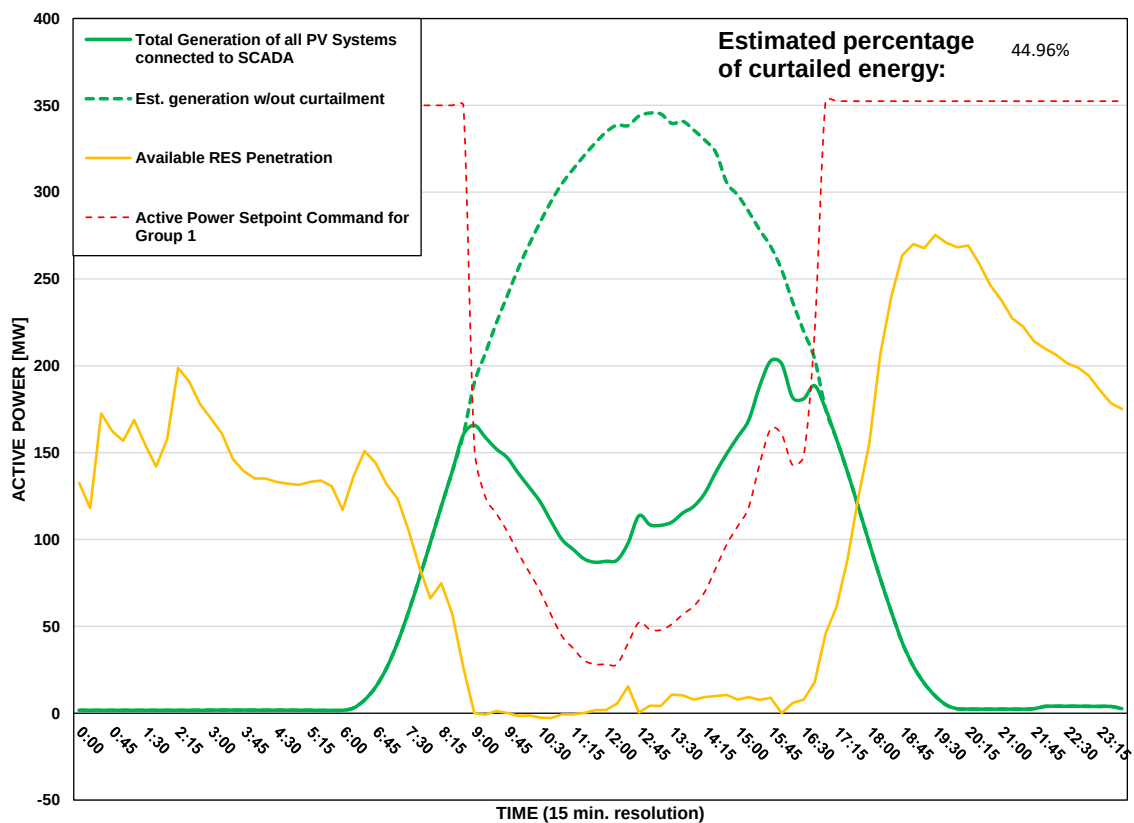


DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION



PV Generation Curtailment Report

Date of Curtailment:	02/08/2026	Cut-off of PV Systems using IoT:
Start of Curtailment (G1 - non Priority)	8:45	Cut-off areas using IoT: PV -ARTICLE 102, PV- NPZEX1
Start of Curtailment (G2 - Priority)	10:30	
End of Curtailment (G1 - non Priority)	17:00	
End of Curtailment (G2 - Priority)	15:00	
Instruction from TSOC	YES	Start of cut-off: 10:45 End of cut-off: 15:15
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system	
Total Estimated Energy of the day:	2886.8 MWh	
Total Estimated Curtailed Energy:	1780.3 MWh	Total Est. Energy of the cut-off PV systems using IoT: 15.1MWh
Percentage of Curtailed Energy:	61.67%	

Scada PVs Generation on 02/08/2026 (curtailment time: 08:45 - 17:00)

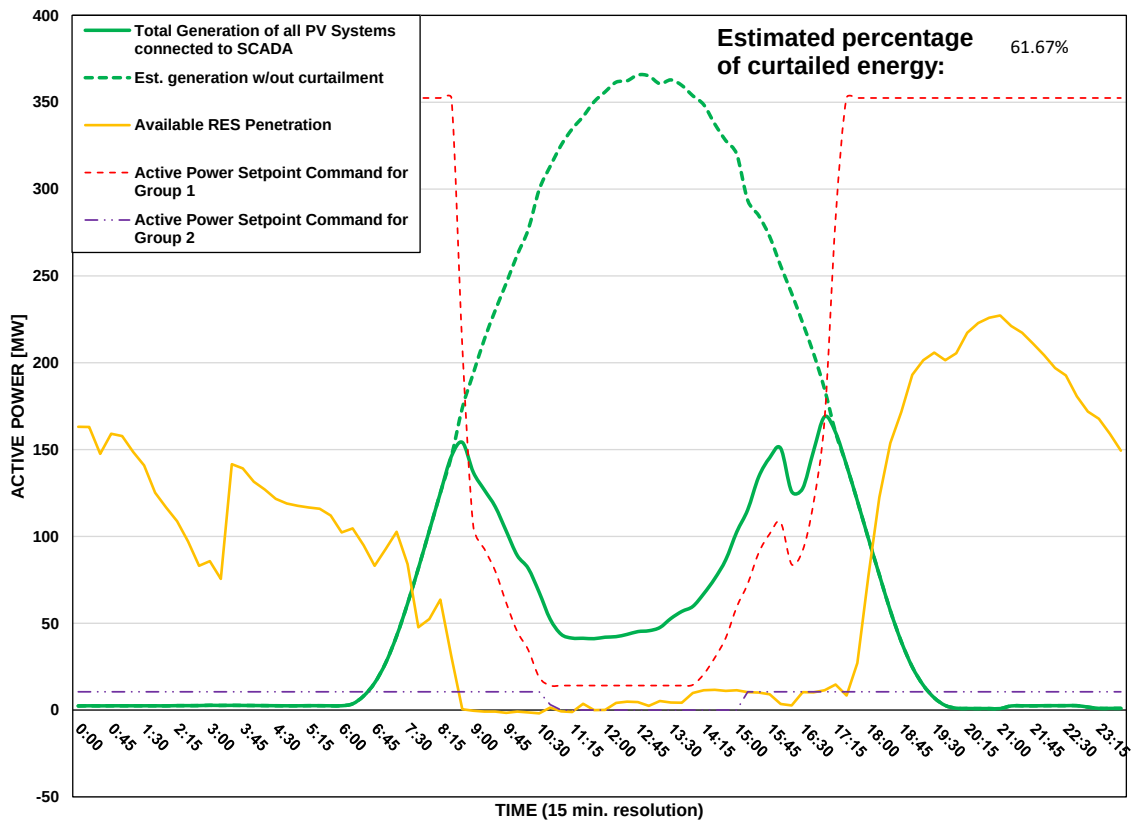

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	03/08/2026
Start of Curtailment (G1 - non Priority)	9:30
End of Curtailment (G1 - non Priority)	15:30
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2827.8 MWh
Total Estimated Curtailed Energy:	802.3 MWh
Percentage of Curtailed Energy:	28.38%

Scada PVs Generation on 03/08/2026 (curtailment time: 09:30 - 15:30)

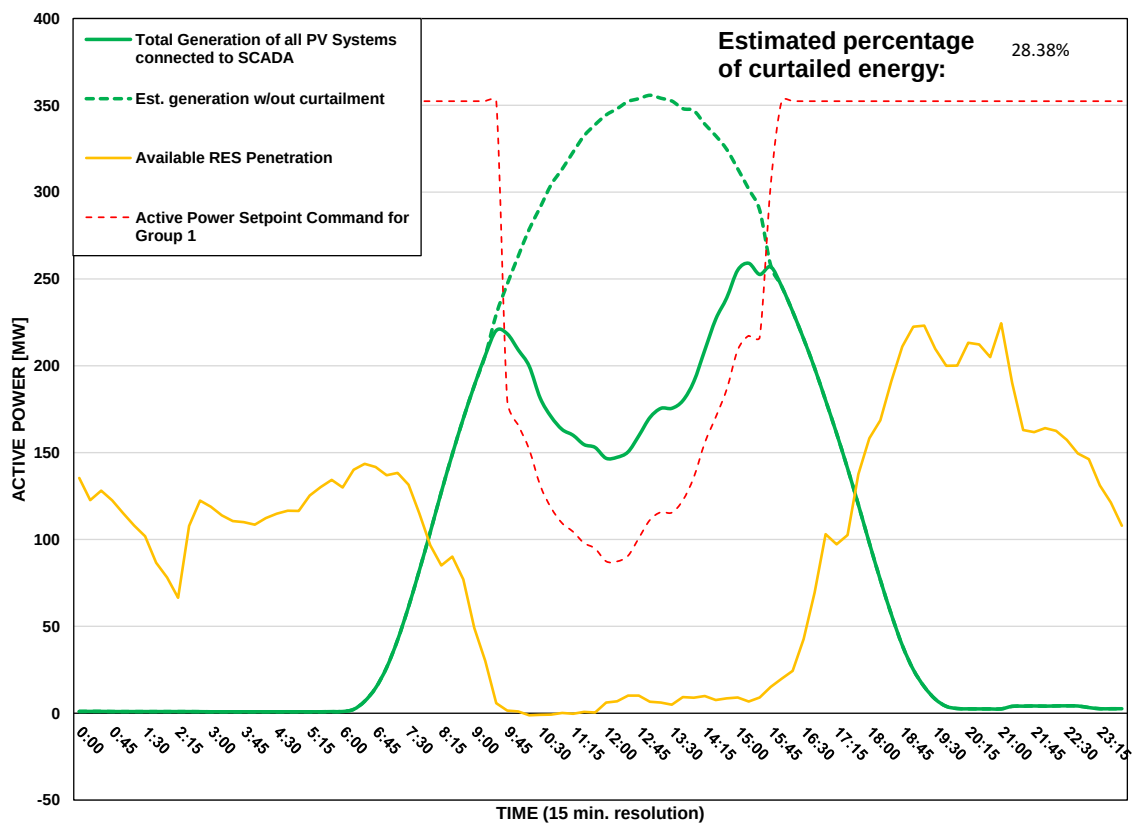

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	04/08/2026
Start of Curtailment (G1 - non Priority)	9:30
End of Curtailment (G1 - non Priority)	15:30
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2771.7 MWh
Total Estimated Curtailed Energy:	820.7 MWh
Percentage of Curtailed Energy:	29.61%

Scada PVs Generation on 04/08/2026 (curtailment time: 09:30 - 15:30)

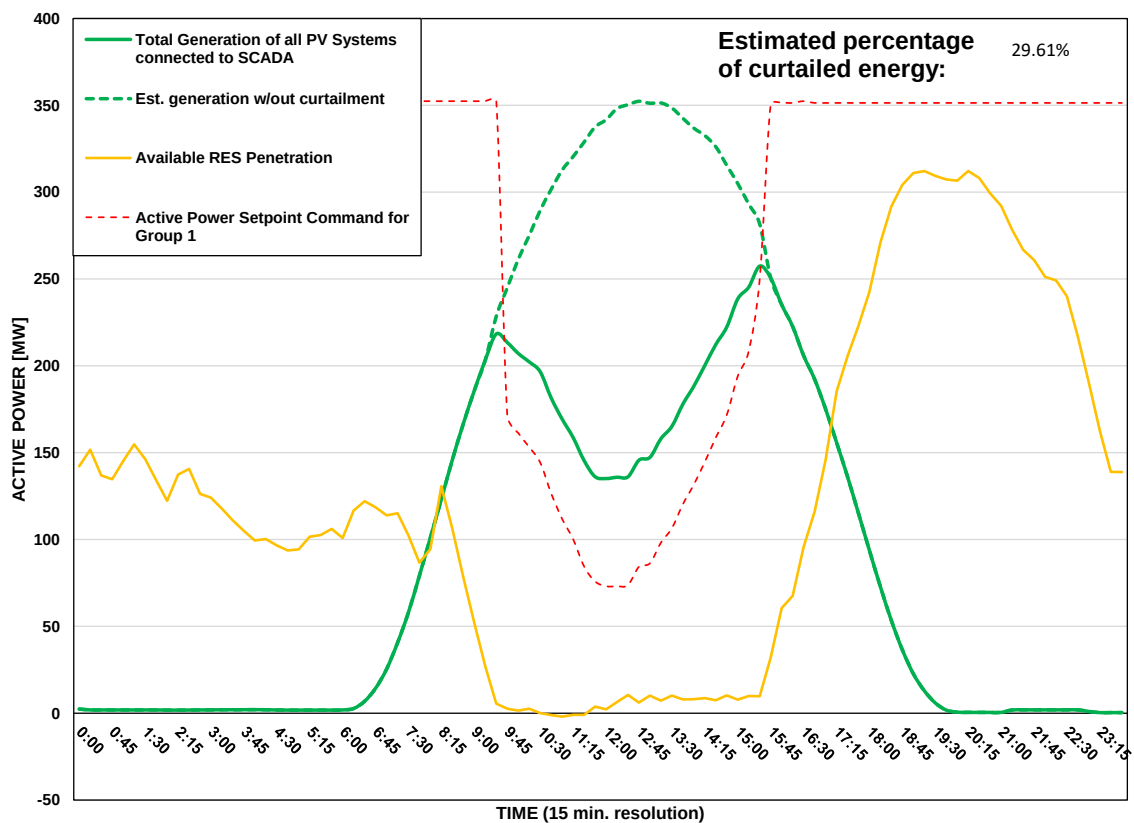

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	05/08/2026
Start of Curtailment (G1 - non Priority)	9:30
End of Curtailment (G1 - non Priority)	15:30
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2739.1 MWh
Total Estimated Curtailed Energy:	744.2 MWh
Percentage of Curtailed Energy:	27.17%

Scada PVs Generation on 05/08/2026 (curtailment time: 09:30 - 15:30)

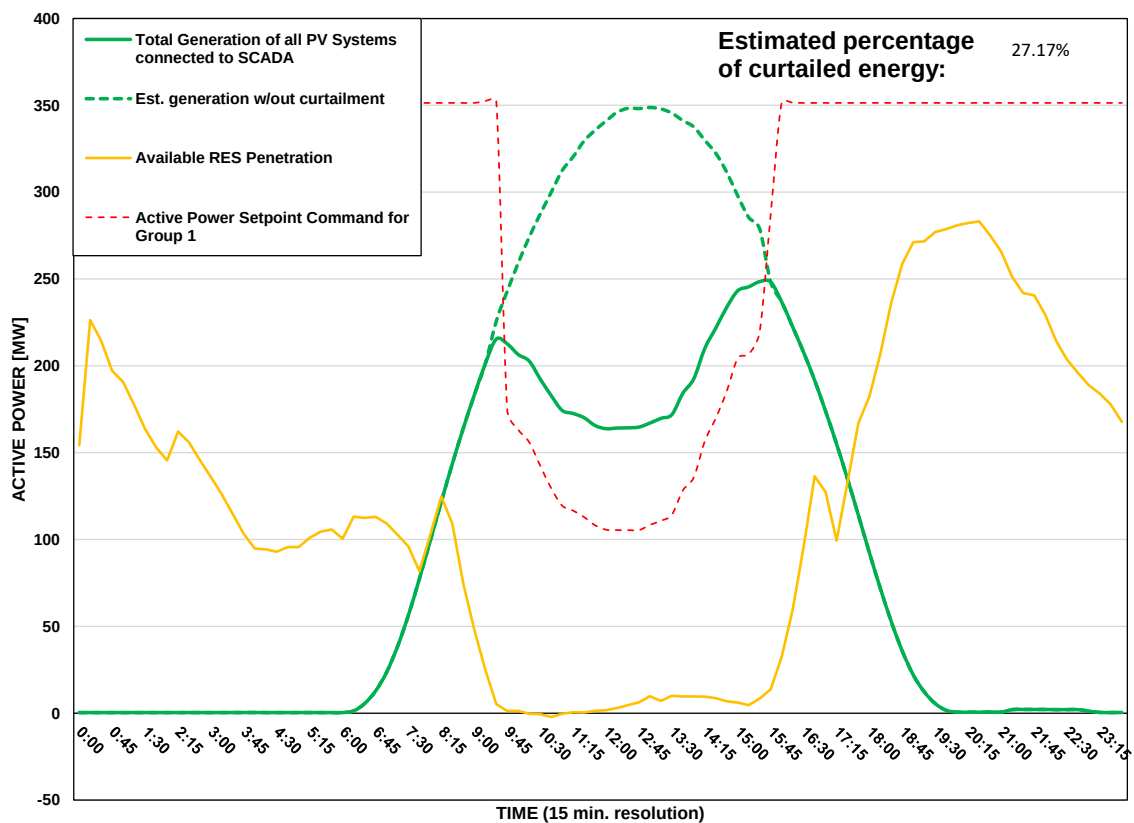

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	06/08/2026
Start of Curtailment (G1 - non Priority)	9:45
End of Curtailment (G1 - non Priority)	15:15
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2648.9 MWh
Total Estimated Curtailed Energy:	617.7 MWh
Percentage of Curtailed Energy:	23.32%

Scada PVs Generation on 06/08/2026 (curtailment time: 09:45 - 15:15)

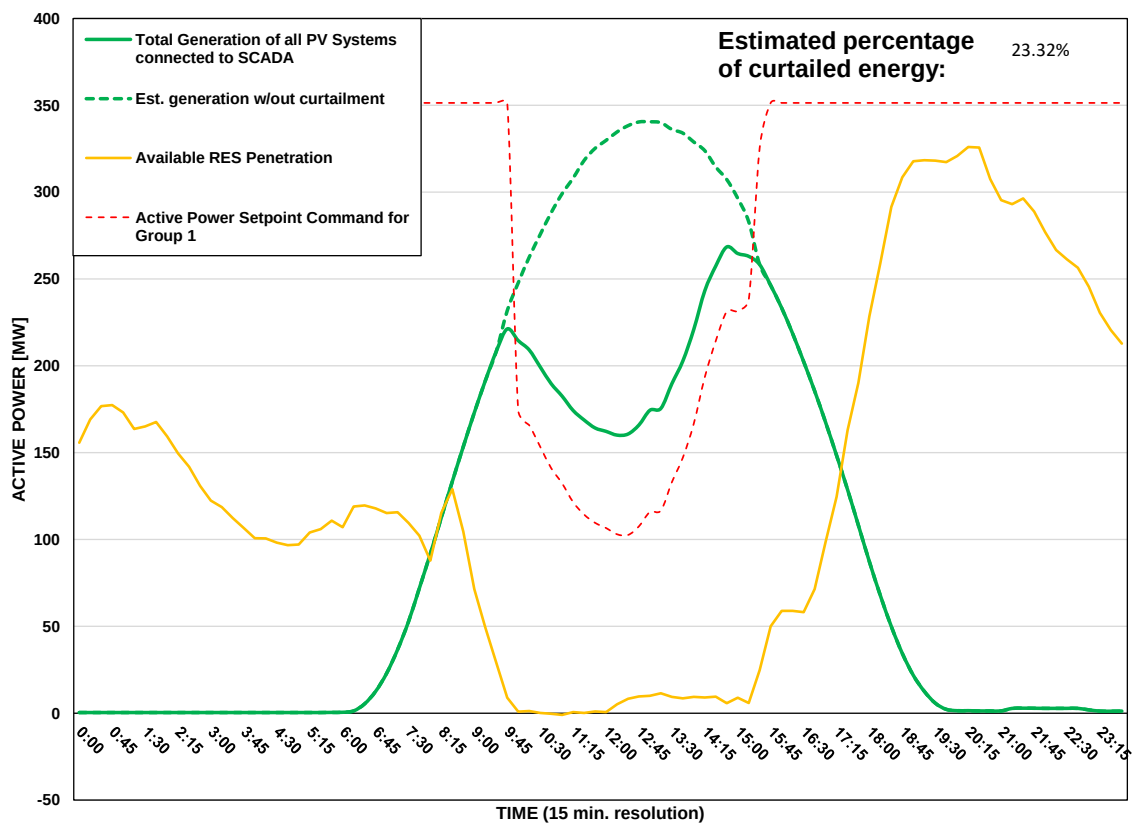

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	07/08/2026
Start of Curtailment (G1 - non Priority)	10:15
End of Curtailment (G1 - non Priority)	14:30
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2563.5 MWh
Total Estimated Curtailed Energy:	356.6 MWh
Percentage of Curtailed Energy:	13.91%

Scada PVs Generation on 07/08/2026 (curtailment time: 10:15 - 14:30)

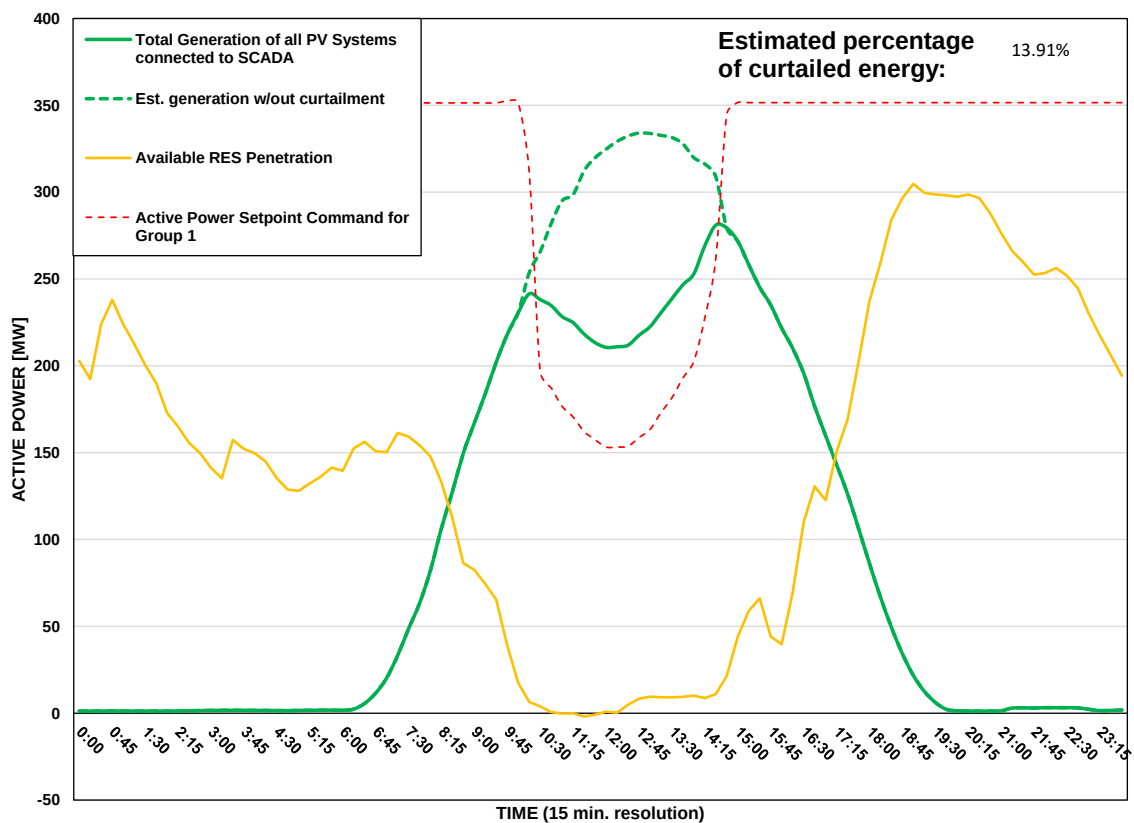

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	08/08/2026
Start of Curtailment (G1 - non Priority)	10:00
End of Curtailment (G1 - non Priority)	15:00
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2580.3 MWh
Total Estimated Curtailed Energy:	529.8 MWh
Percentage of Curtailed Energy:	20.53%

Scada PVs Generation on 08/08/2026 (curtailment time: 10:00 - 15:00)

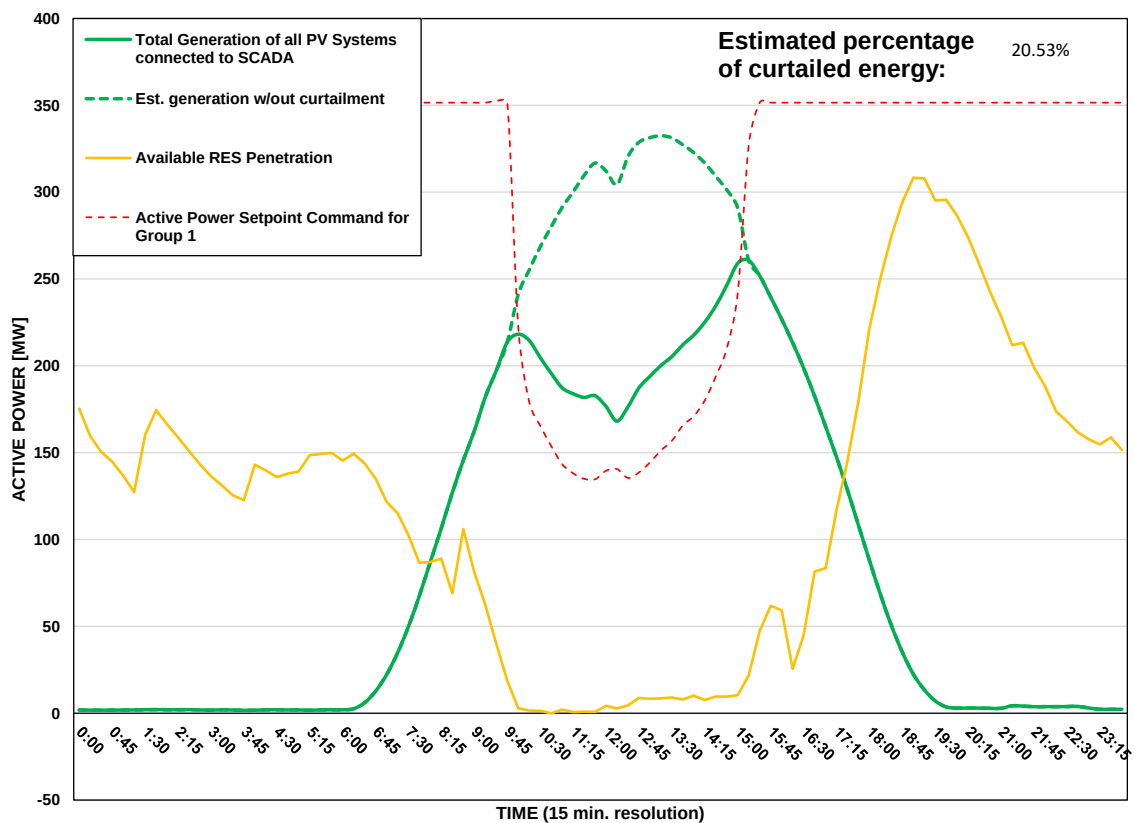


DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION



PV Generation Curtailment Report

Date of Curtailment:	09/08/2026	Cut-off of PV Systems using IoT:
Start of Curtailment (G1 - non Priority)	8:45	Cut-off areas using IoT: PV -ARTICLE 102, PV- NPZEX1
Start of Curtailment (G2 - Priority)	11:00	
End of Curtailment (G1 - non Priority)	16:00	
End of Curtailment (G2 - Priority)	13:15	
Instruction from TSOC	YES	Start of cut-off: 11:15 End of cut-off: 13:30
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system	
Total Estimated Energy of the day:	2707.1 MWh	
Total Estimated Curtailed Energy:	1424.1 MWh	Total Est. Energy of the cut-off PV systems using IoT: 7.2MWh
Percentage of Curtailed Energy:	52.61%	

Scada PVs Generation on 09/08/2026 (curtailment time: 08:45 - 16:00)

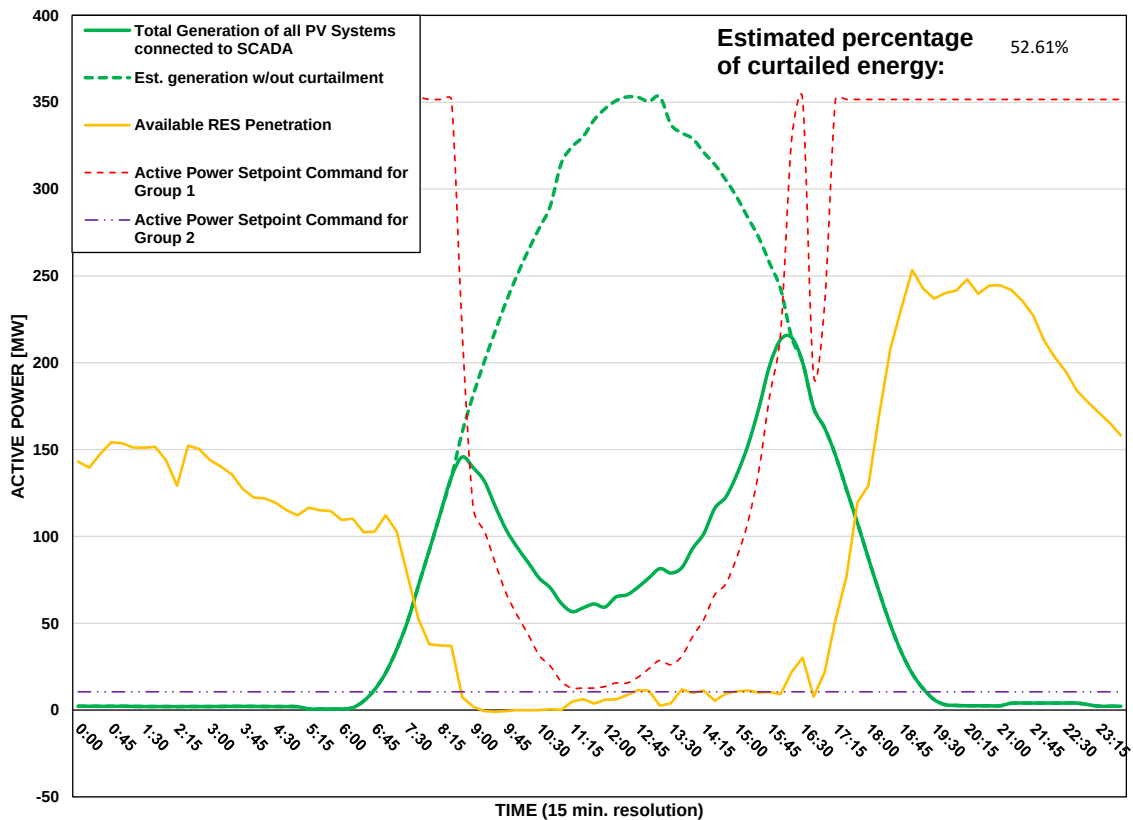

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	10/08/2026
Start of Curtailment (G1 - non Priority)	10:30
End of Curtailment (G1 - non Priority)	14:30
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2615.1 MWh
Total Estimated Curtailed Energy:	305.8 MWh
Percentage of Curtailed Energy:	11.69%

Scada PVs Generation on 10/08/2026 (curtailment time: 10:30 - 14:30)

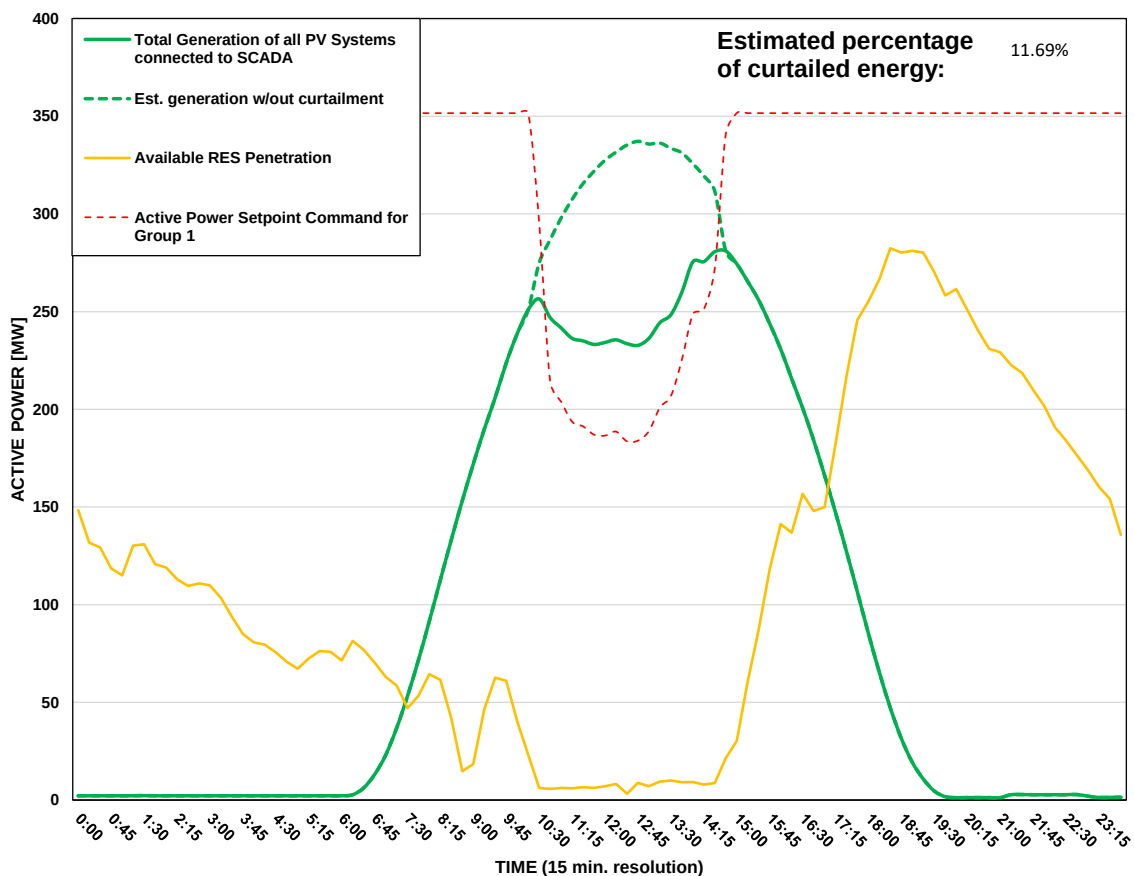

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	11/08/2026
Start of Curtailment (G1 - non Priority)	10:45
End of Curtailment (G1 - non Priority)	15:00
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2515.6 MWh
Total Estimated Curtailed Energy:	259.9 MWh
Percentage of Curtailed Energy:	10.33%

Scada PVs Generation on 11/08/2026 (curtailment time: 10:45 - 15:00)

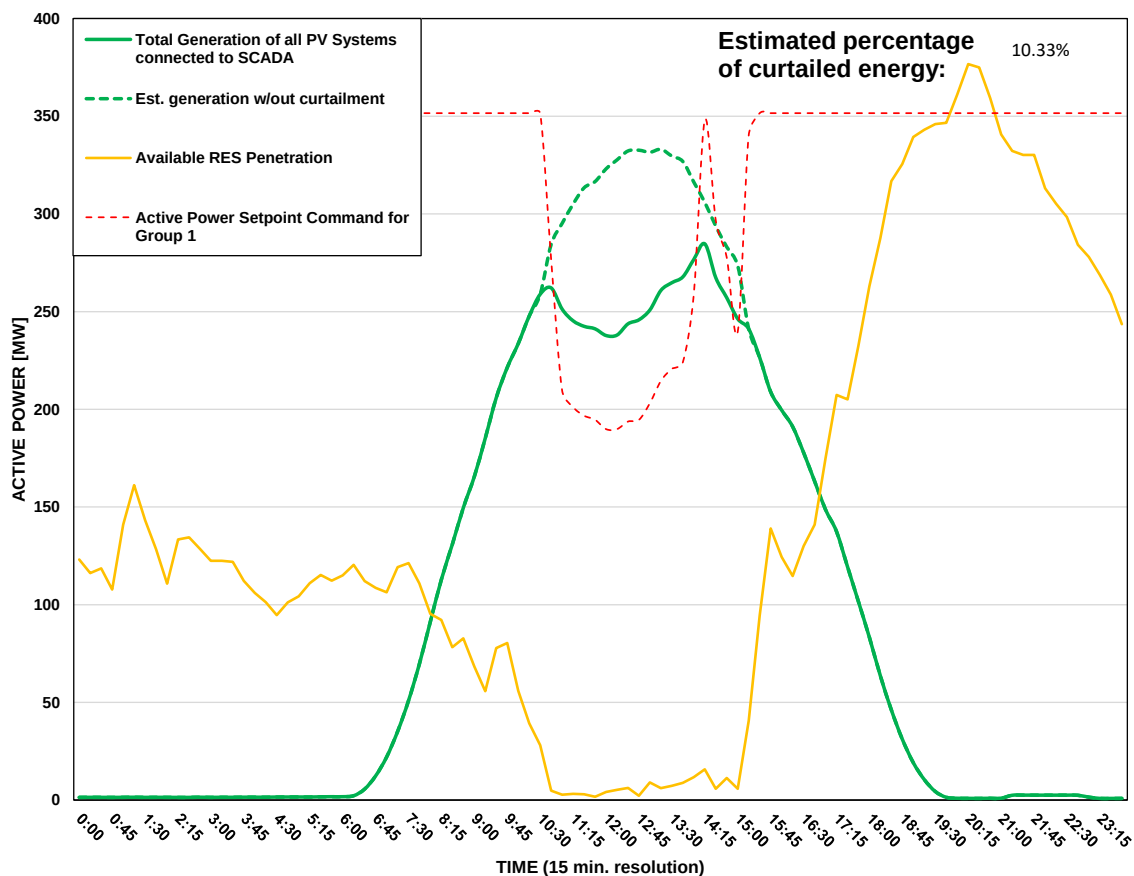

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	12/08/2026
Start of Curtailment (G1 - non Priority)	9:45
End of Curtailment (G1 - non Priority)	14:30
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2558.9 MWh
Total Estimated Curtailed Energy:	490.6 MWh
Percentage of Curtailed Energy:	19.17%

Scada PVs Generation on 12/08/2026 (curtailment time: 09:45 - 14:30)

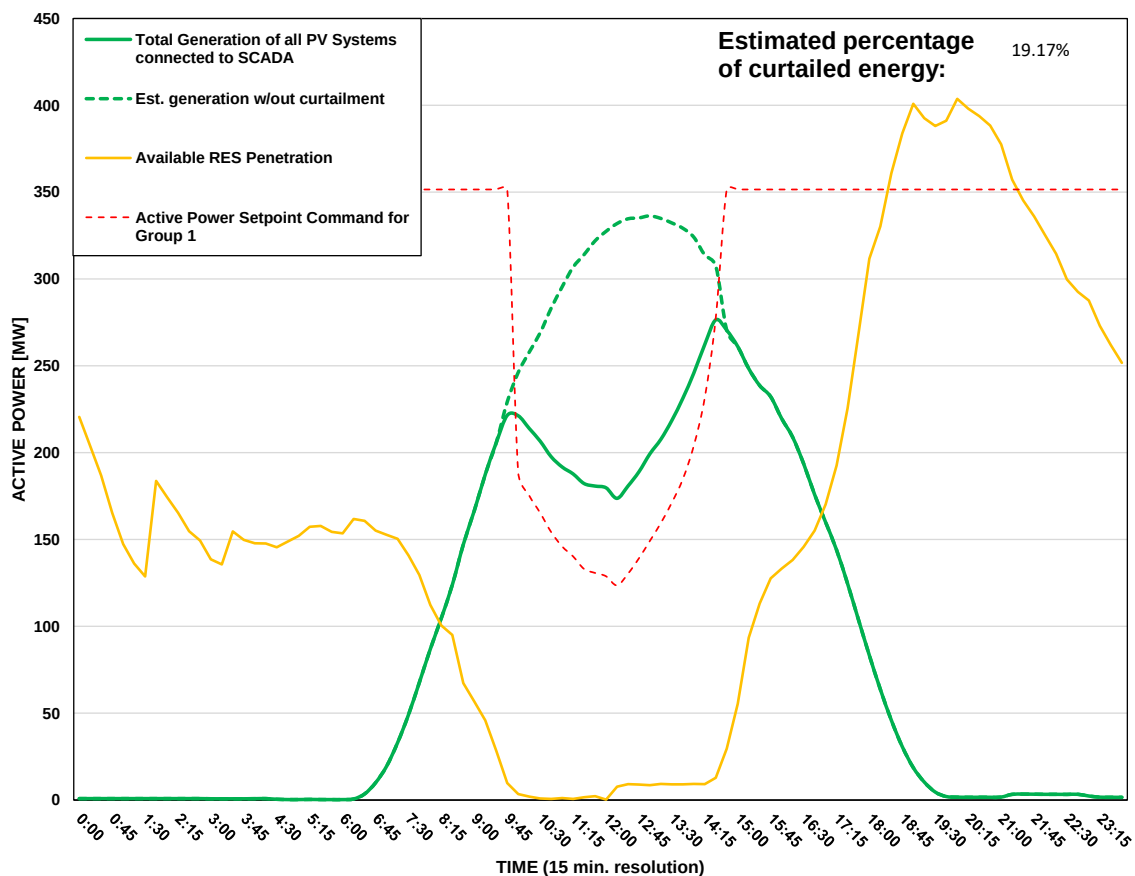

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	13/08/2026
Start of Curtailment (G1 - non Priority)	10:00
End of Curtailment (G1 - non Priority)	14:45
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2522 MWh
Total Estimated Curtailed Energy:	469.9 MWh
Percentage of Curtailed Energy:	18.63%

Scada PVs Generation on 13/08/2026 (curtailment time: 10:00 - 14:45)

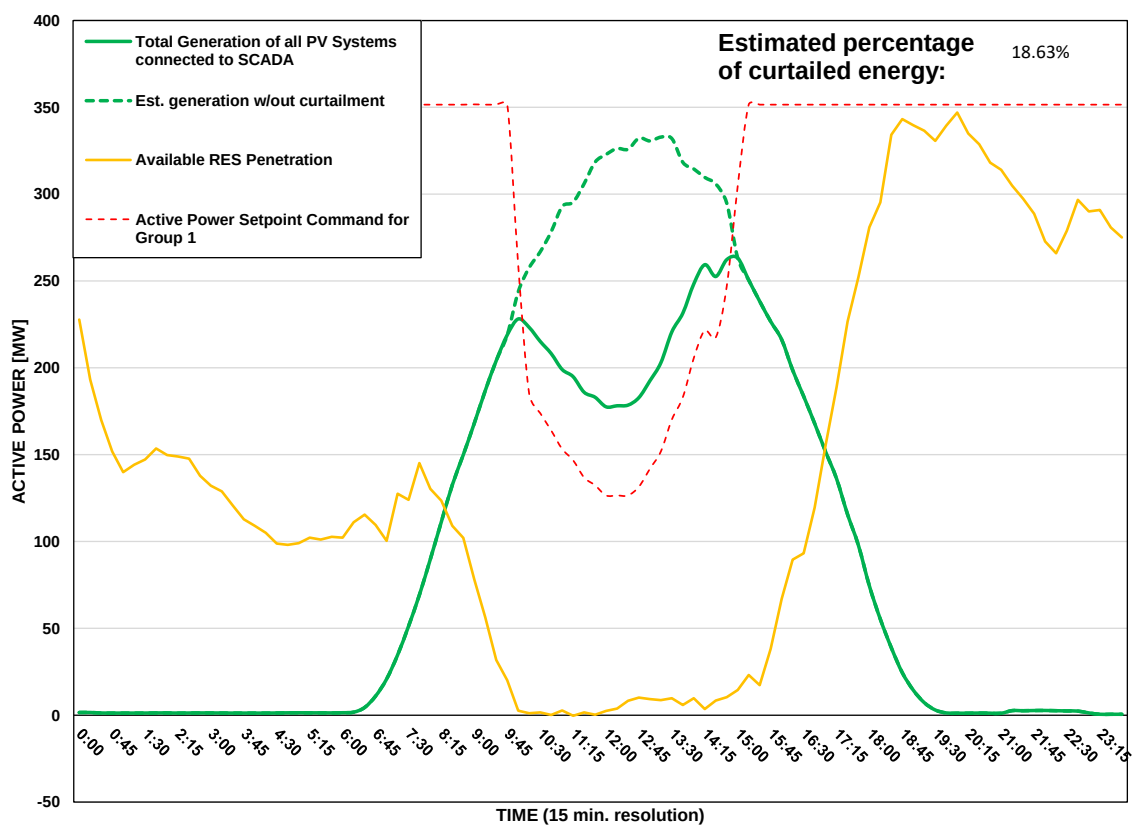

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	14/08/2026
Start of Curtailment (G1 - non Priority)	10:45
End of Curtailment (G1 - non Priority)	14:15
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2025.2 MWh
Total Estimated Curtailed Energy:	298.5 MWh
Percentage of Curtailed Energy:	14.75%

Scada PVs Generation on 14/08/2026 (curtailment time: 10:45 - 14:15)

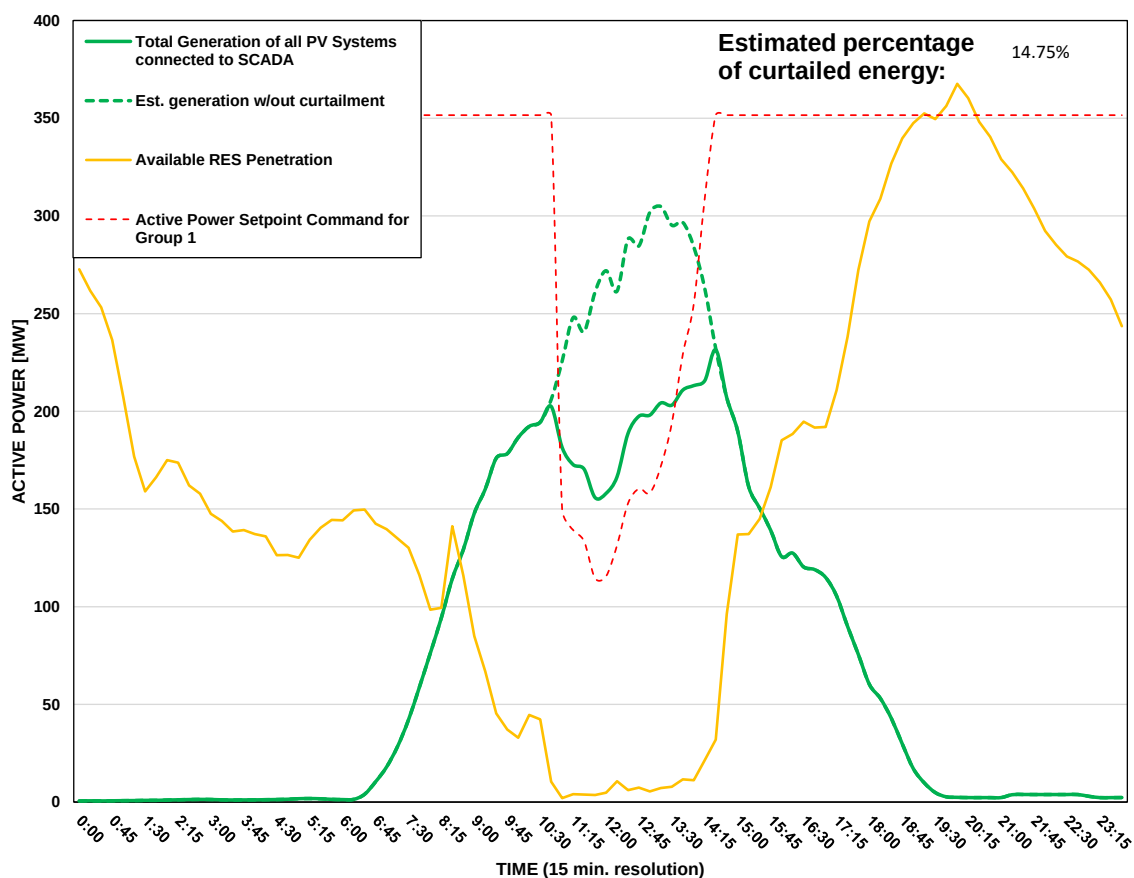

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	15/08/2026
Start of Curtailment (G1 - non Priority)	8:30
End of Curtailment (G1 - non Priority)	16:30
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2348 MWh
Total Estimated Curtailed Energy:	1032 MWh
Percentage of Curtailed Energy:	43.95%

Scada PVs Generation on 15/08/2026 (curtailment time: 08:30 - 16:30)

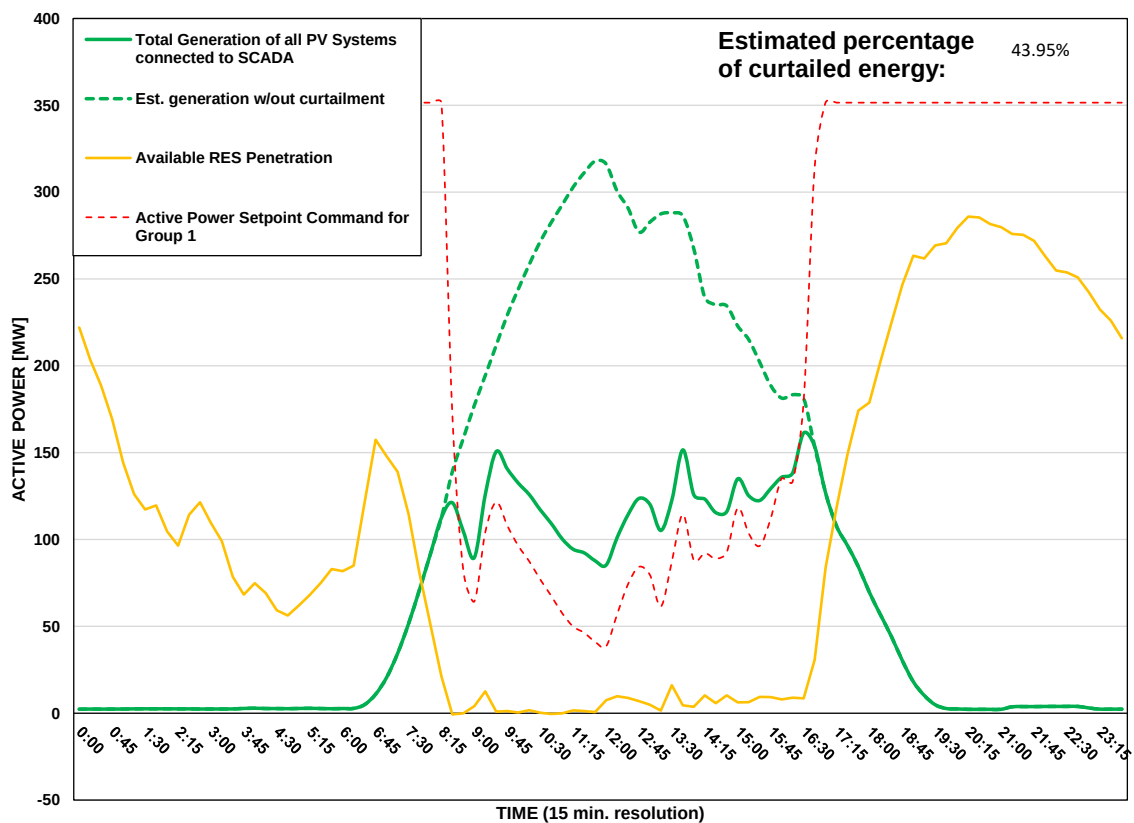


DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION



PV Generation Curtailment Report

Date of Curtailment:	16/08/2026	Cut-off of PV Systems using IoT:
Start of Curtailment (G1 - non Priority)	8:45	Cut-off areas using IoT: PV -ARTICLE 102, PV- NPZEX1
Start of Curtailment (G2 - Priority)	11:15	
End of Curtailment (G1 - non Priority)	17:00	
End of Curtailment (G2 - Priority)	13:30	
Instruction from TSOC	YES	Start of cut-off: 11:15 End of cut-off: 18:15
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system	
Total Estimated Energy of the day:	2398.8 MWh	
Total Estimated Curtailed Energy:	1200.1 MWh	Total Est. Energy of the cut-off PV systems using IoT: 14.6MWh
Percentage of Curtailed Energy:	50.03%	

Scada PVs Generation on 16/08/2026 (curtailment time: 08:45 - 17:00)

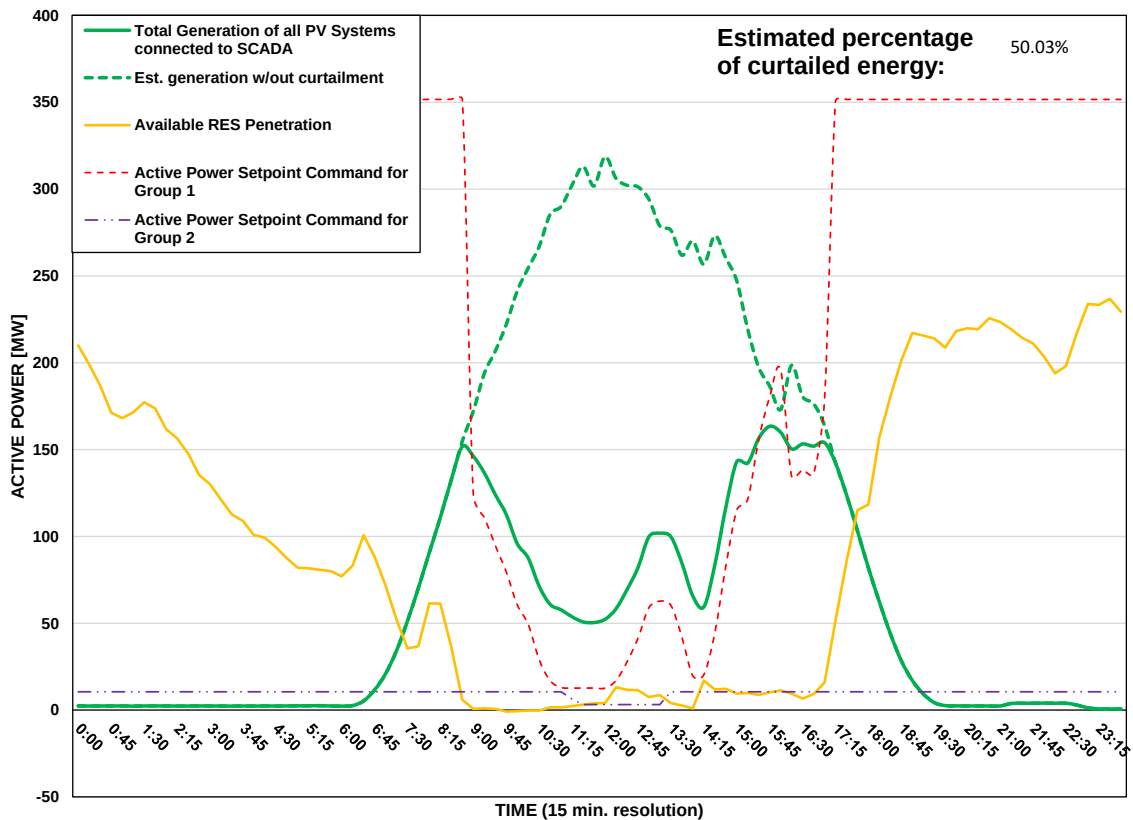


DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION



PV Generation Curtailment Report

Date of Curtailment:	17/08/2026	Cut-off of PV Systems using IoT:
Start of Curtailment (G1 - non Priority)	9:30	Cut-off areas using IoT: PV -ARTICLE 102, PV- NPZEX1
Start of Curtailment (G2 - Priority)	11:30	
End of Curtailment (G1 - non Priority)	13:45	
End of Curtailment (G2 - Priority)	12:00	
Instruction from TSOC	YES	Start of cut-off: 07:15 End of cut-off: 13:00
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system	
Total Estimated Energy of the day:	2020.7 MWh	
Total Estimated Curtailed Energy:	629.2 MWh	Total Est. Energy of the cut-off PV systems using IoT: 5.2MWh
Percentage of Curtailed Energy:	31.16%	

Scada PVs Generation on 17/08/2026 (curtailment time: 09:30 - 13:45)

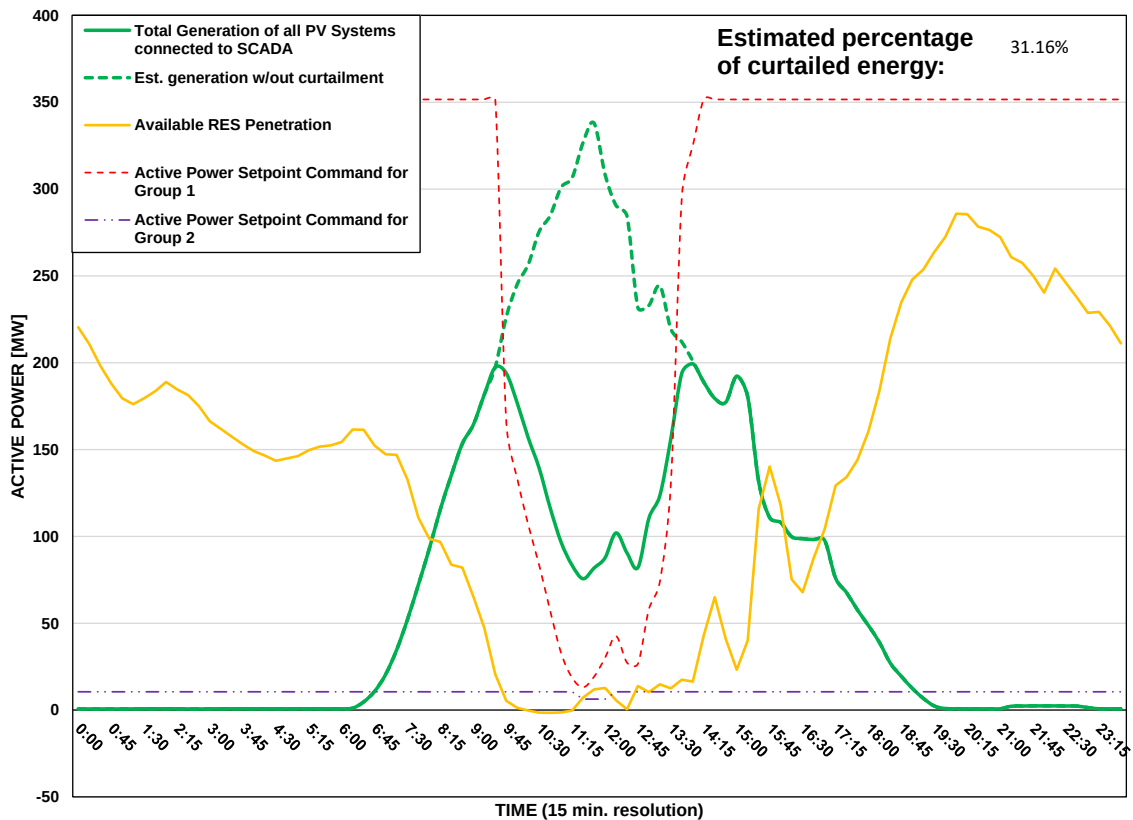

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	18/08/2026
Start of Curtailment (G1 - non Priority)	9:15
End of Curtailment (G1 - non Priority)	16:30
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2419.1 MWh
Total Estimated Curtailed Energy:	938.7 MWh
Percentage of Curtailed Energy:	38.8%

Scada PVs Generation on 18/08/2026 (curtailment time: 09:15 - 16:30)

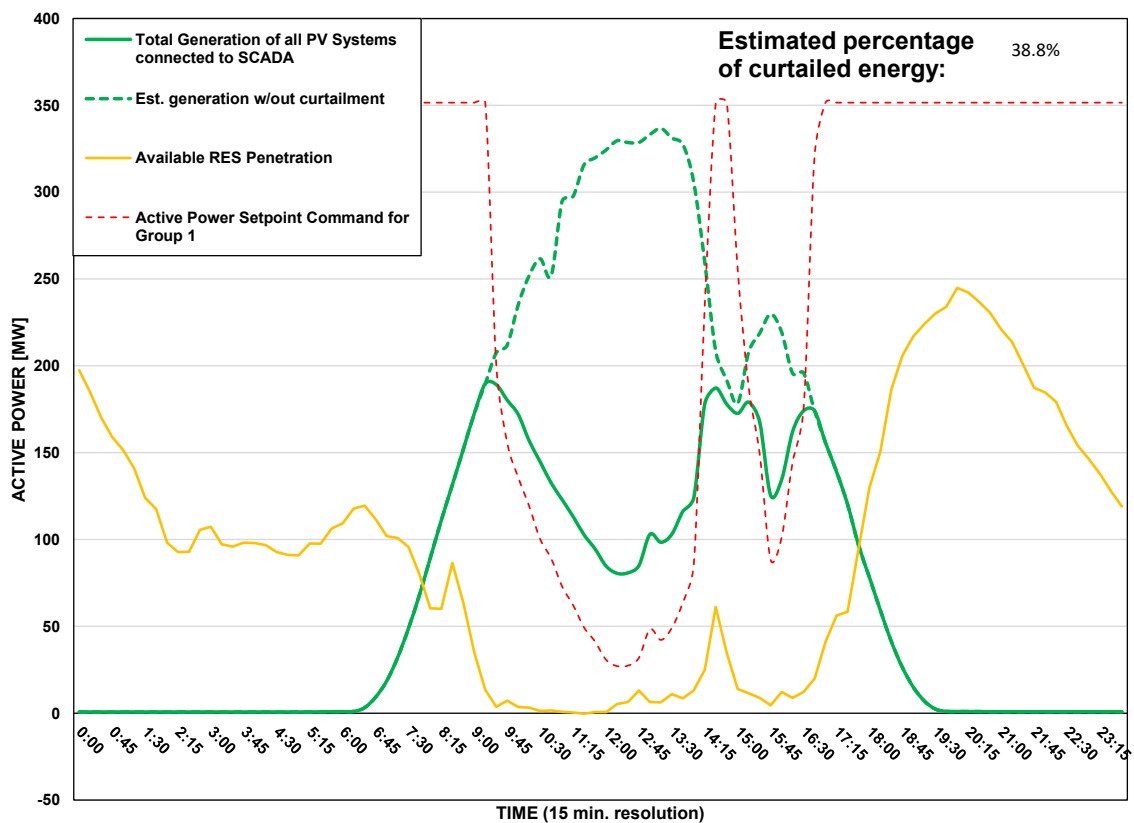

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	19/08/2026
Start of Curtailment (G1 - non Priority)	9:15
End of Curtailment (G1 - non Priority)	15:15
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2502.3 MWh
Total Estimated Curtailed Energy:	871.9 MWh
Percentage of Curtailed Energy:	34.85%

Scada PVs Generation on 19/08/2026 (curtailment time: 09:15 - 15:15)

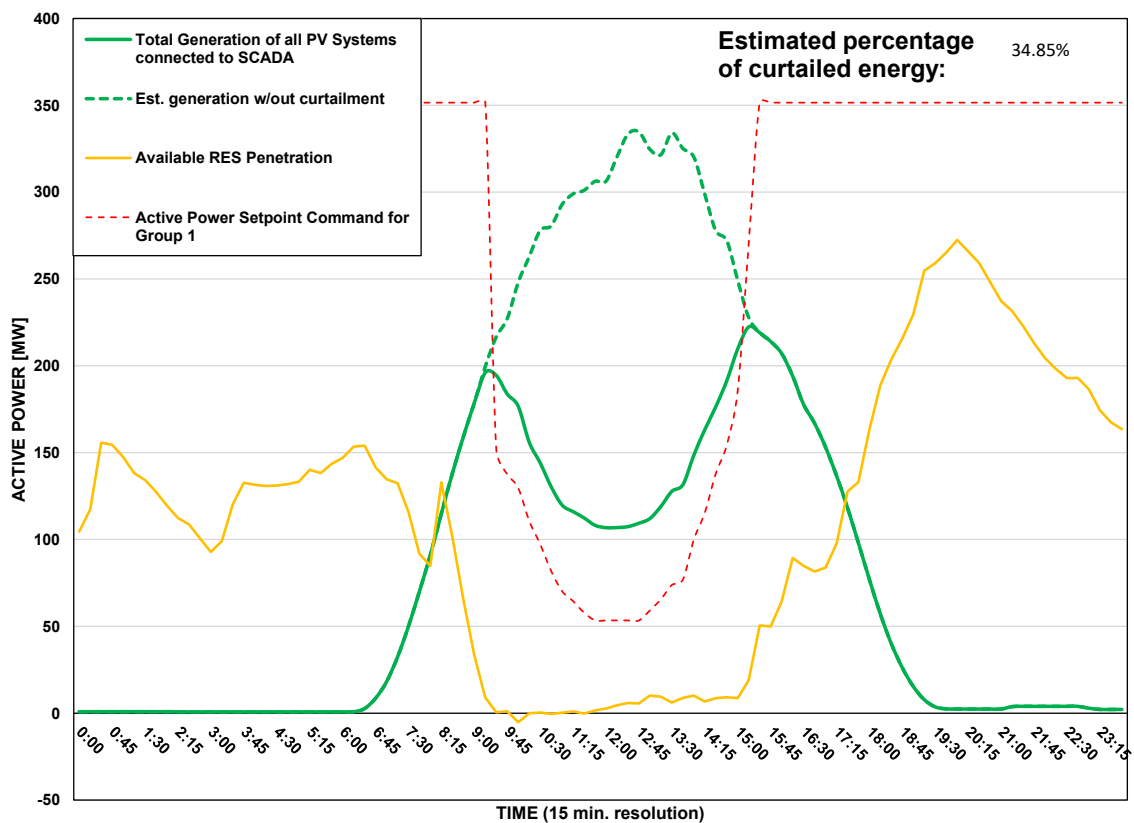

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	20/08/2026
Start of Curtailment (G1 - non Priority)	9:15
End of Curtailment (G1 - non Priority)	15:15
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2670.9 MWh
Total Estimated Curtailed Energy:	831.8 MWh
Percentage of Curtailed Energy:	31.14%

Scada PVs Generation on 20/08/2026 (curtailment time: 09:15 - 15:15)

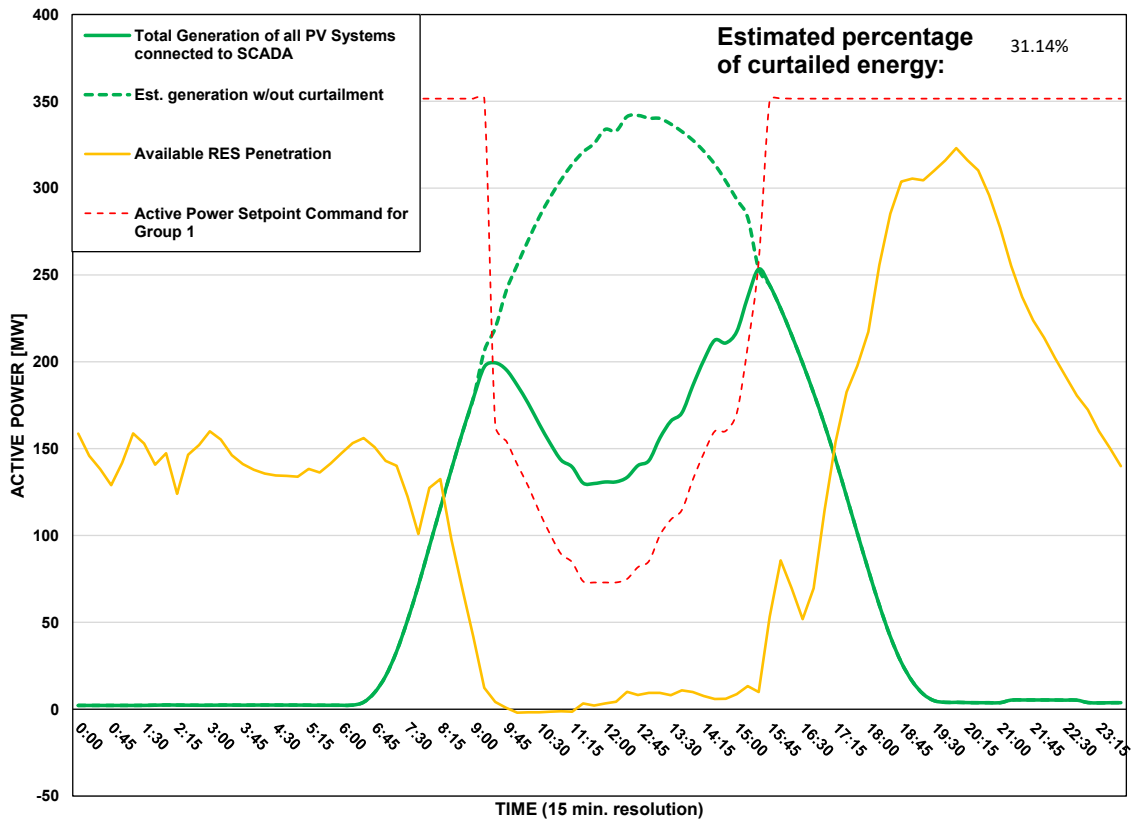

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	21/08/2026
Start of Curtailment (G1 - non Priority)	10:00
End of Curtailment (G1 - non Priority)	14:30
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2601.8 MWh
Total Estimated Curtailed Energy:	536.4 MWh
Percentage of Curtailed Energy:	20.62%

Scada PVs Generation on 21/08/2026 (curtailment time: 10:00 - 14:30)

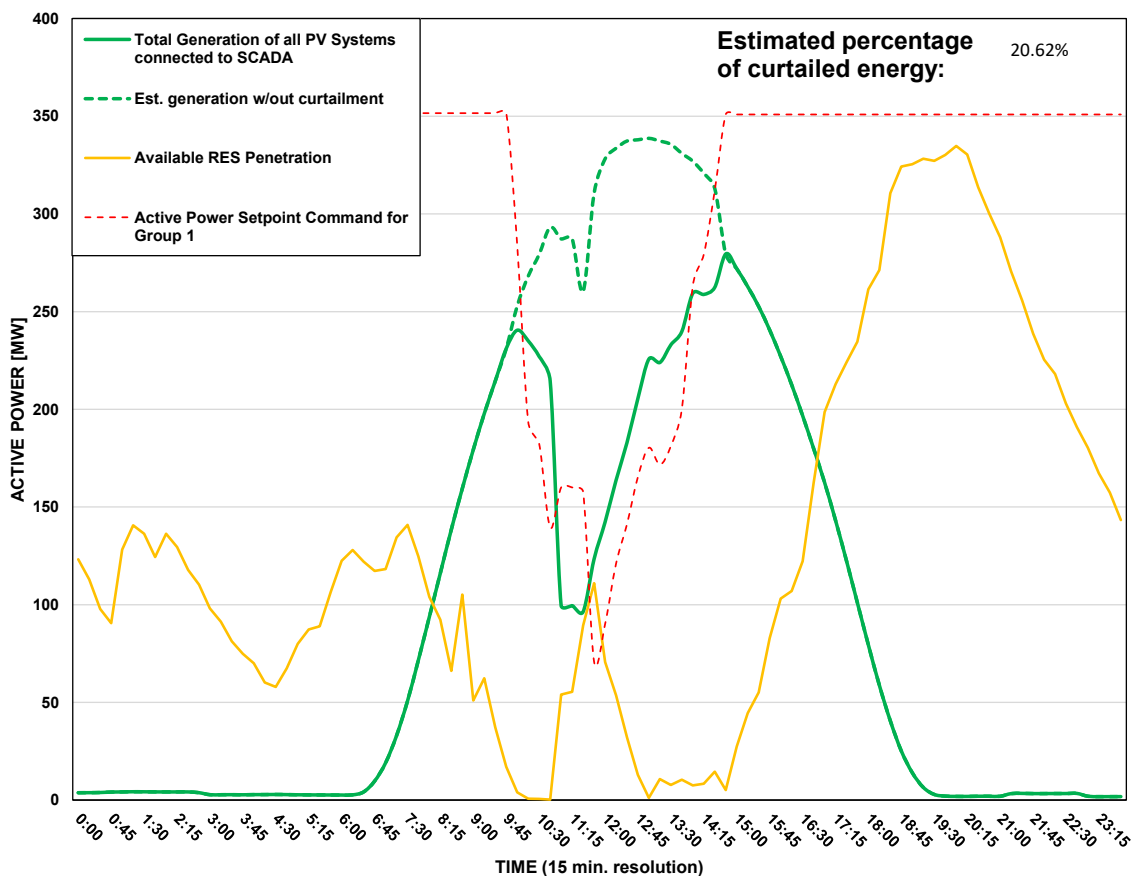

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	22/08/2026
Start of Curtailment (G1 - non Priority)	9:30
End of Curtailment (G1 - non Priority)	15:00
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2645.8 MWh
Total Estimated Curtailed Energy:	677.2 MWh
Percentage of Curtailed Energy:	25.59%

Scada PVs Generation on 22/08/2026 (curtailment time: 09:30 - 15:00)

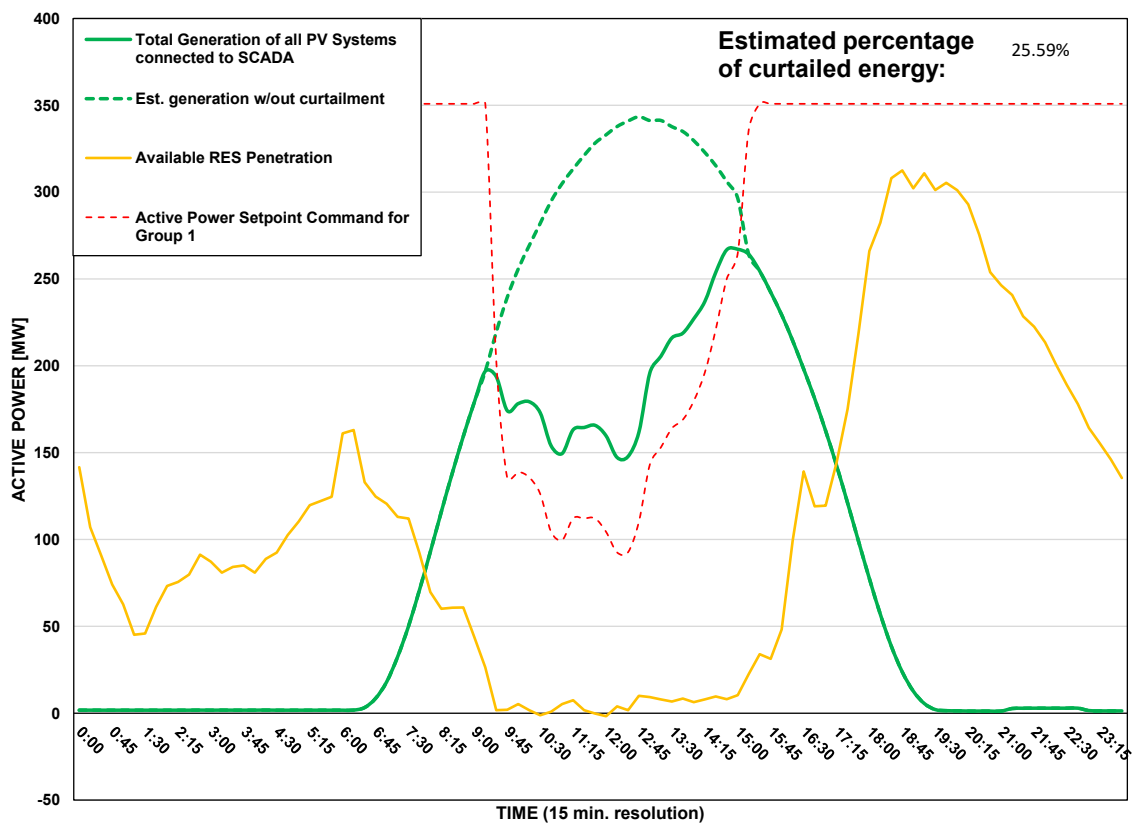


DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION



PV Generation Curtailment Report

Date of Curtailment:	23/08/2026	Cut-off of PV Systems using IoT:
Start of Curtailment (G1 - non Priority)	8:30	Cut-off areas using IoT: PV -ARTICLE 102, PV- NPZEX1
Start of Curtailment (G2 - Priority)	11:30	
End of Curtailment (G1 - non Priority)	16:00	
End of Curtailment (G2 - Priority)	12:45	
Instruction from TSOC	YES	Start of cut-off: 11:30 End of cut-off: 12:45
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system	
Total Estimated Energy of the day:	2683.6 MWh	
Total Estimated Curtailed Energy:	1410.3 MWh	Total Est. Energy of the cut-off PV systems using IoT: 5.5MWh
Percentage of Curtailed Energy:	52.55%	

Scada PVs Generation on 23/08/2026 (curtailment time: 08:30 - 16:00)

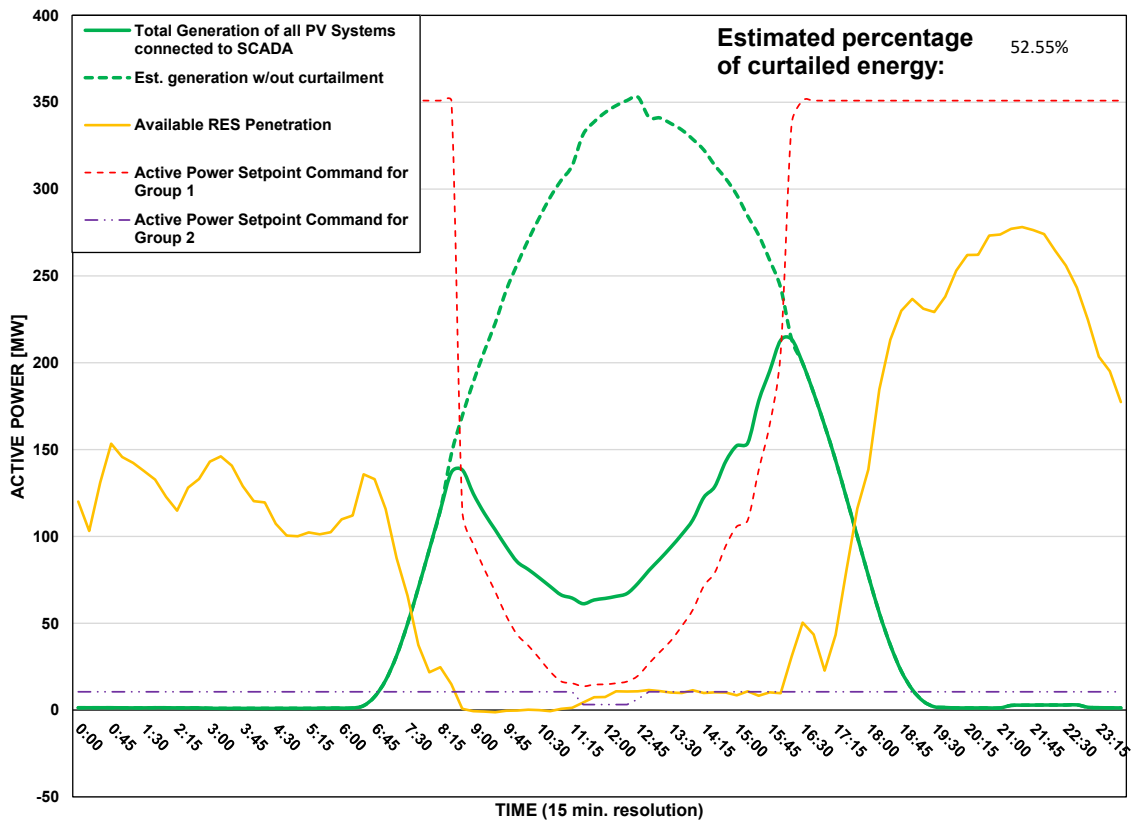

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	24/08/2026
Start of Curtailment (G1 - non Priority)	10:30
End of Curtailment (G1 - non Priority)	14:30
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2481 MWh
Total Estimated Curtailed Energy:	303.9 MWh
Percentage of Curtailed Energy:	12.25%

Scada PVs Generation on 24/08/2026 (curtailment time: 10:30 - 14:30)

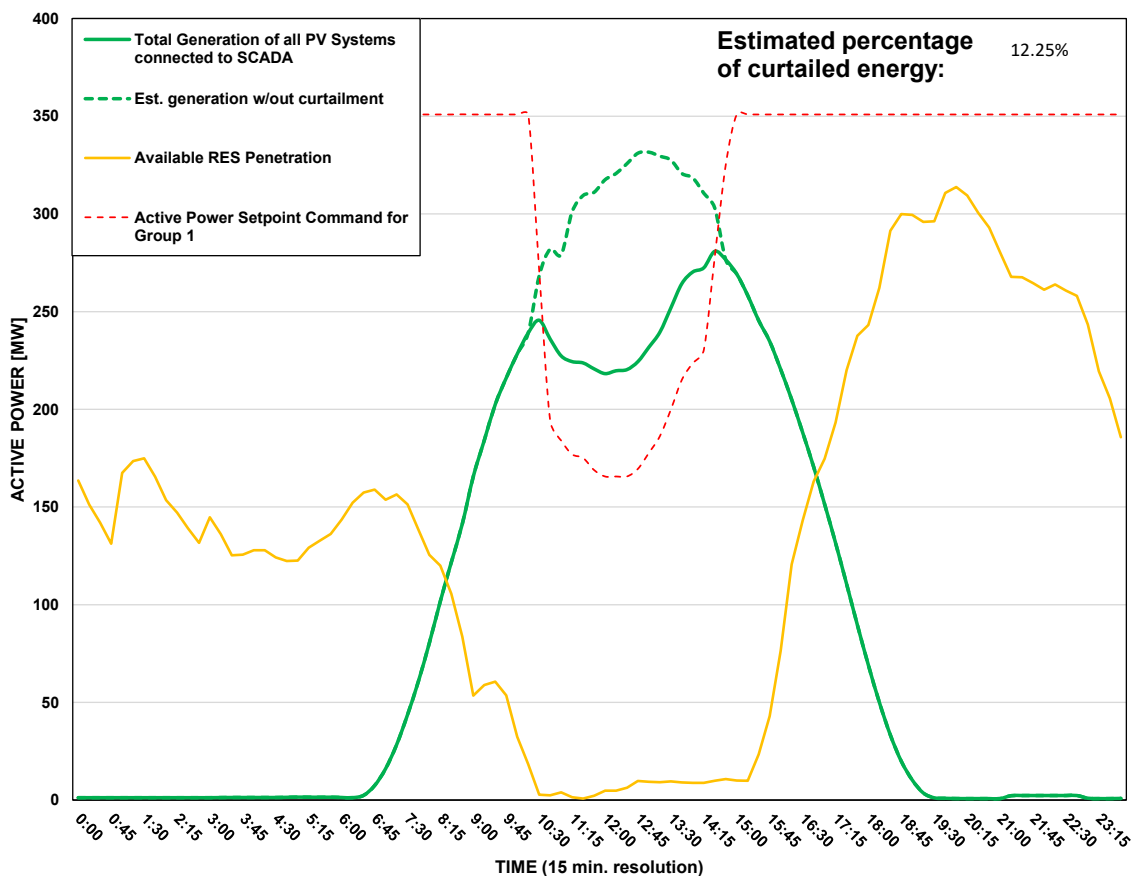

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	25/08/2026
Start of Curtailment (G1 - non Priority)	10:30
End of Curtailment (G1 - non Priority)	14:15
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2501.2 MWh
Total Estimated Curtailed Energy:	236 MWh
Percentage of Curtailed Energy:	9.49%

Scada PVs Generation on 25/08/2026 (curtailment time: 10:30 - 14:15)

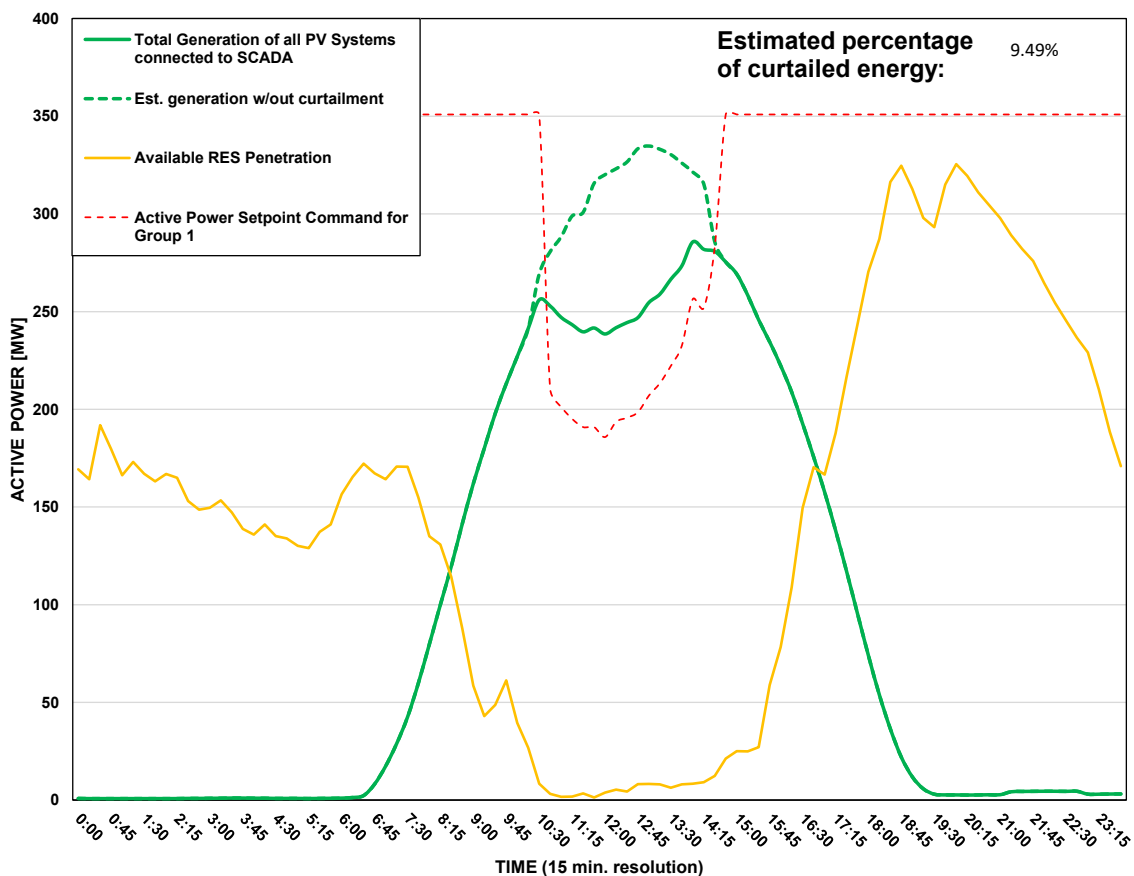

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	26/08/2026
Start of Curtailment (G1 - non Priority)	9:00
End of Curtailment (G1 - non Priority)	15:15
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2597.2 MWh
Total Estimated Curtailed Energy:	715.1 MWh
Percentage of Curtailed Energy:	27.53%

Scada PVs Generation on 26/08/2026 (curtailment time: 09:00 - 15:15)

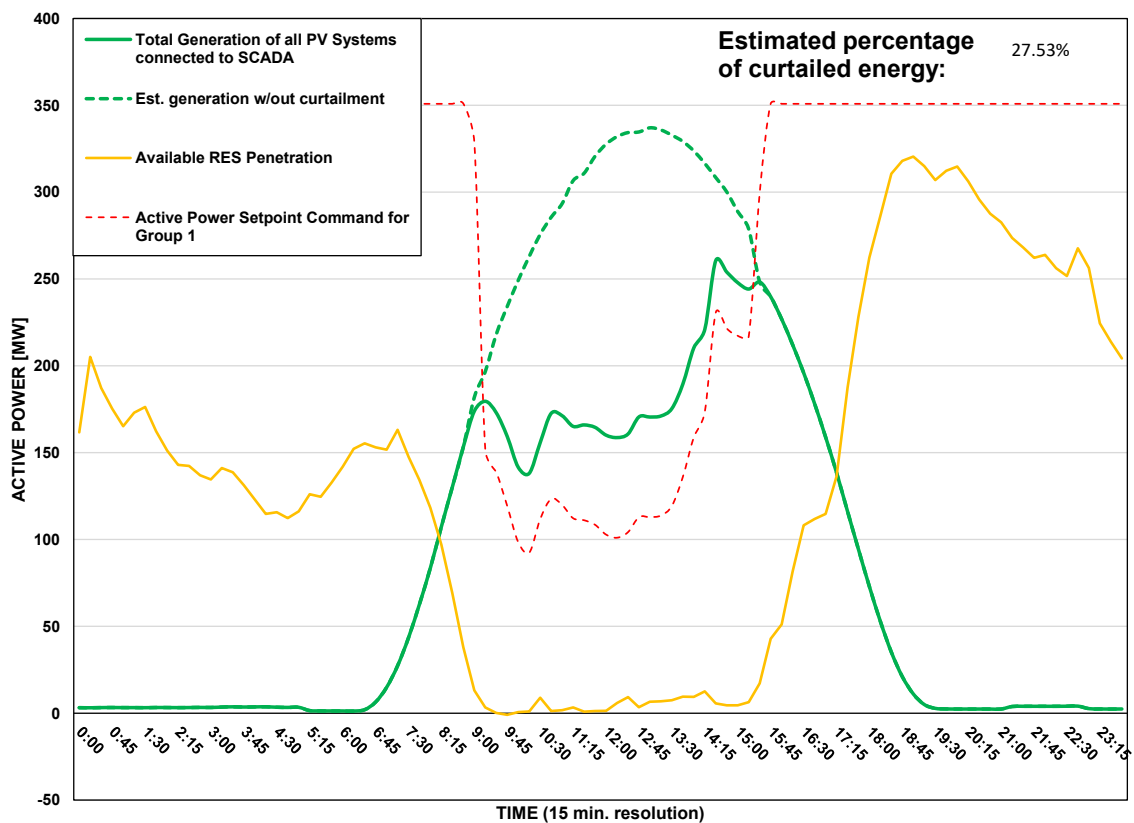

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	27/08/2026
Start of Curtailment (G1 - non Priority)	9:30
End of Curtailment (G1 - non Priority)	14:15
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2470.6 MWh
Total Estimated Curtailed Energy:	546.9 MWh
Percentage of Curtailed Energy:	22.14%

Scada PVs Generation on 27/08/2026 (curtailment time: 09:30 - 14:15)

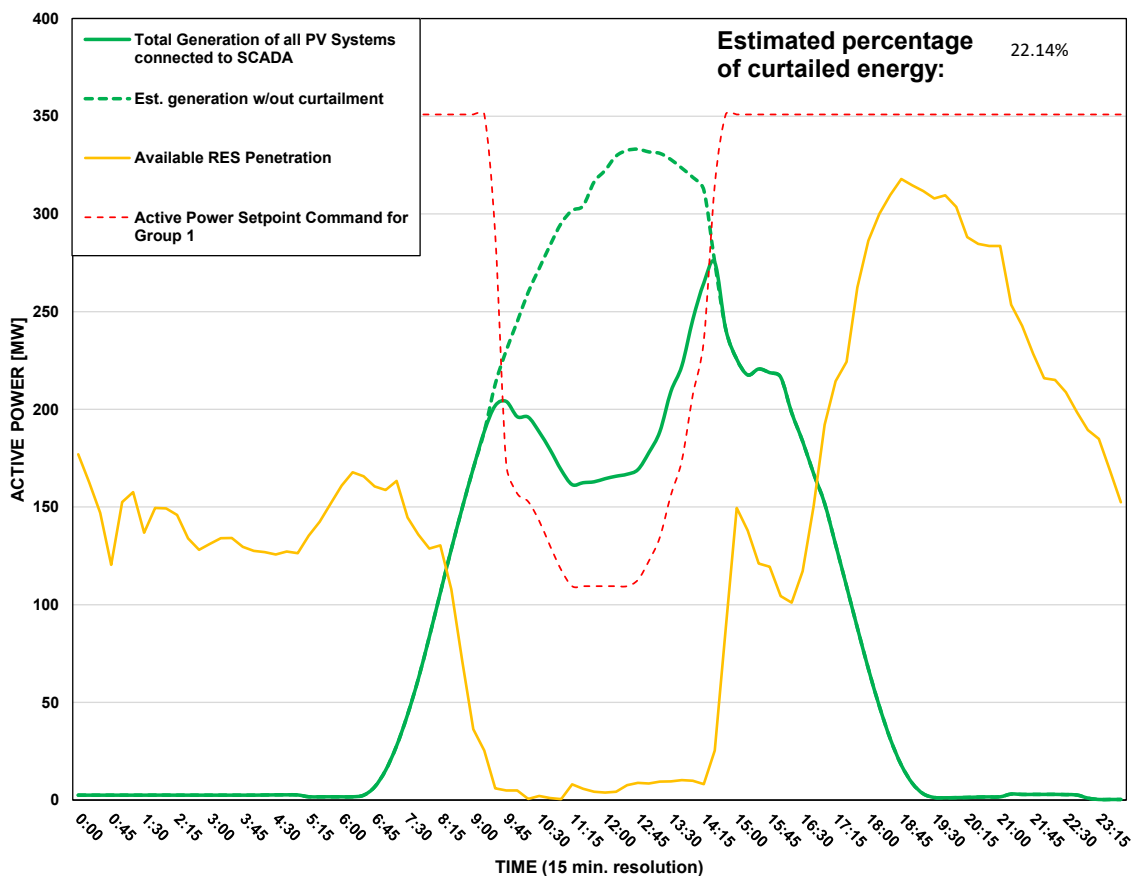

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION




Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	28/08/2026
Start of Curtailment (G1 - non Priority)	10:00
End of Curtailment (G1 - non Priority)	13:45
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2356.9 MWh
Total Estimated Curtailed Energy:	337.4 MWh
Percentage of Curtailed Energy:	14.32%

Scada PVs Generation on 28/08/2026 (curtailment time: 10:00 - 13:45)

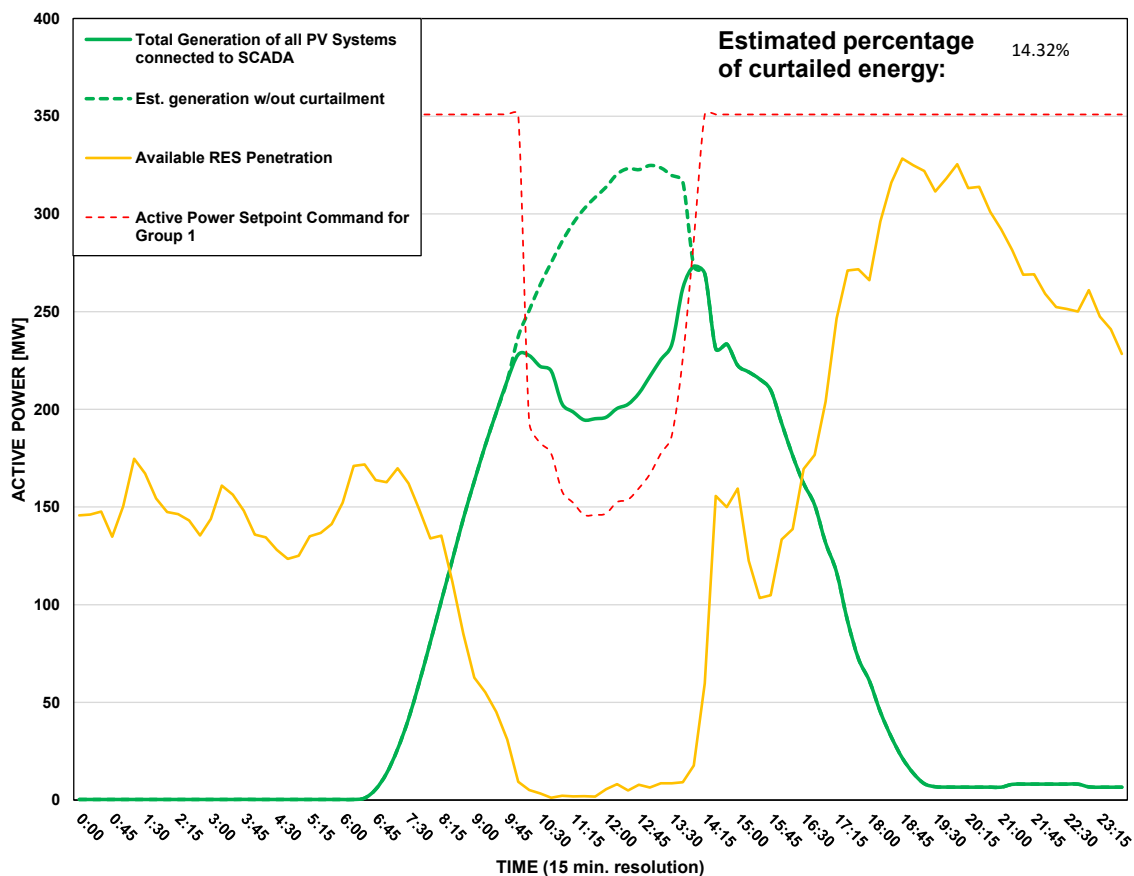


DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION



PV Generation Curtailment Report

Date of Curtailment:	29/08/2026	Cut-off of PV Systems using RIPPLE and IoT:
Start of Curtailment (G1 - non Priority)	9:00	
Start of Curtailment (G2 - Priority)	13:15	Cut-off areas using RIPPLE: NIC 1, NIC 2, NIC 3, LAR 1, LAR 2, LIM 1, LIM 2, PAF 1, PAF 2 Cut-off areas using IoT: PV-NIC1, PV-NIC2, PV-NIC3, PV-NIC4, PV-LCA/FAM1, PV-LCA/FAM2, PV-LIM3, PV-PAF3, PV -ARTICLE 102, PV- NPZEX1
End of Curtailment (G1 - non Priority)	18:30	
End of Curtailment (G2 - Priority)	18:30	
Instruction from TSOC	YES	Start of cut-off: 15:15 End of cut-off: 17:45
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system	
Total Estimated Energy of the day:	1289.5 MWh	Total Est. Energy of the cut-off PV systems using RIPPLE: 230.1MWh
Total Estimated Curtailed Energy:	805.8 MWh	Total Est. Energy of the cut-off PV systems using IoT: 88.6MWh
Percentage of Curtailed Energy:	62.5%	

Scada PVs Generation on 29/08/2026 (curtailment time: 09:00 - 18:30)

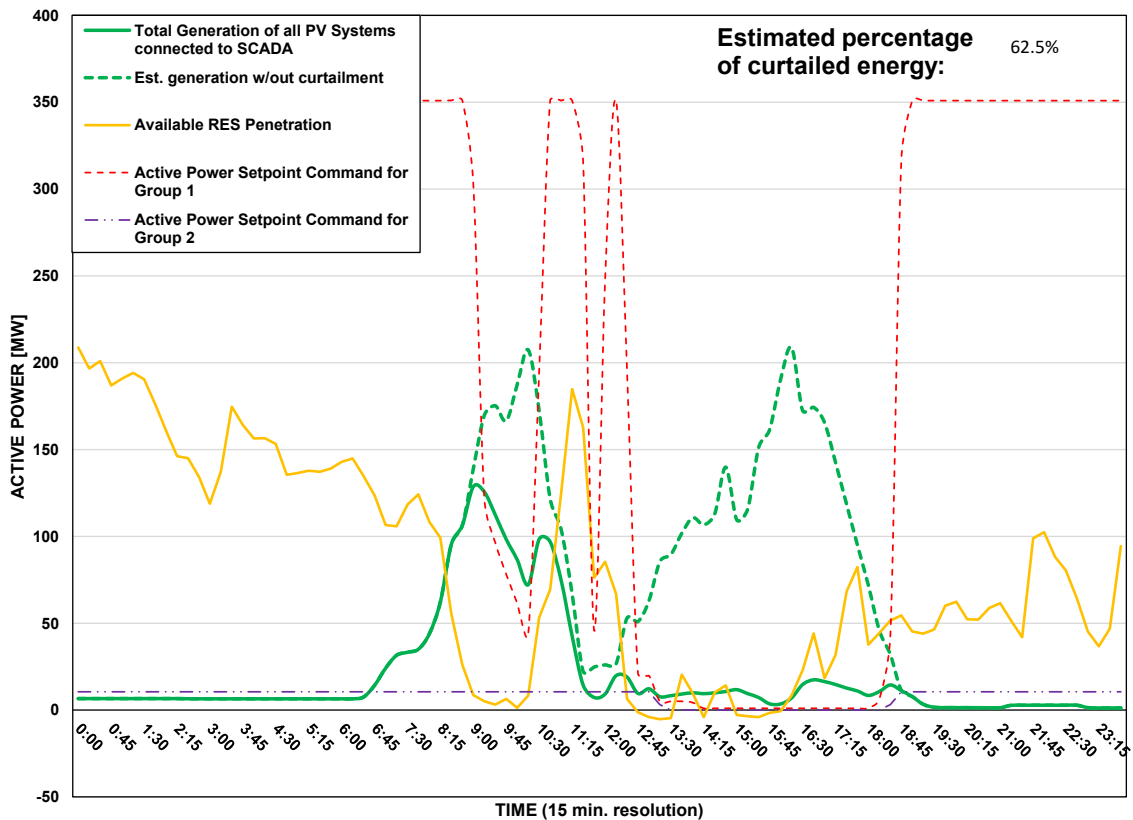


DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION



PV Generation Curtailment Report

Date of Curtailment:	30/08/2026	Cut-off of PV Systems using RIPPLE and IoT:
Start of Curtailment (G1 - non Priority)	8:00	
Start of Curtailment (G2 - Priority)	8:30	Cut-off areas using RIPPLE: NIC 1, NIC 2, NIC 3, LAR 1, LAR 2, LIM 1, LIM 2, PAF 1, PAF 2 Cut-off areas using IoT: PV-NIC2, PV-NIC3, PV-NIC5, PV-NIC6, PV-LCA/FAM2, PV-LCA/FAM3, PV-LCA/FAM4, PV-LIM1, PV-LIM3, PV-PAF1, PV-PAF3, PV - ARTICLE 102, PV -PROD 1, PV- NPZEX1
End of Curtailment (G1 - non Priority)	16:45	
End of Curtailment (G2 - Priority)	15:45	
Instruction from TSOC	YES	Start of cut-off: 08:45 End of cut-off: 16:00
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system	
Total Estimated Energy of the day:	2525.7 MWh	Total Est. Energy of the cut-off PV systems using RIPPLE: 567.6MWh
Total Estimated Curtailed Energy:	1796.1 MWh	Total Est. Energy of the cut-off PV systems using IoT: 727MWh
Percentage of Curtailed Energy:	71.11%	

Scada PVs Generation on 30/08/2026 (curtailment time: 08:00 - 16:45)

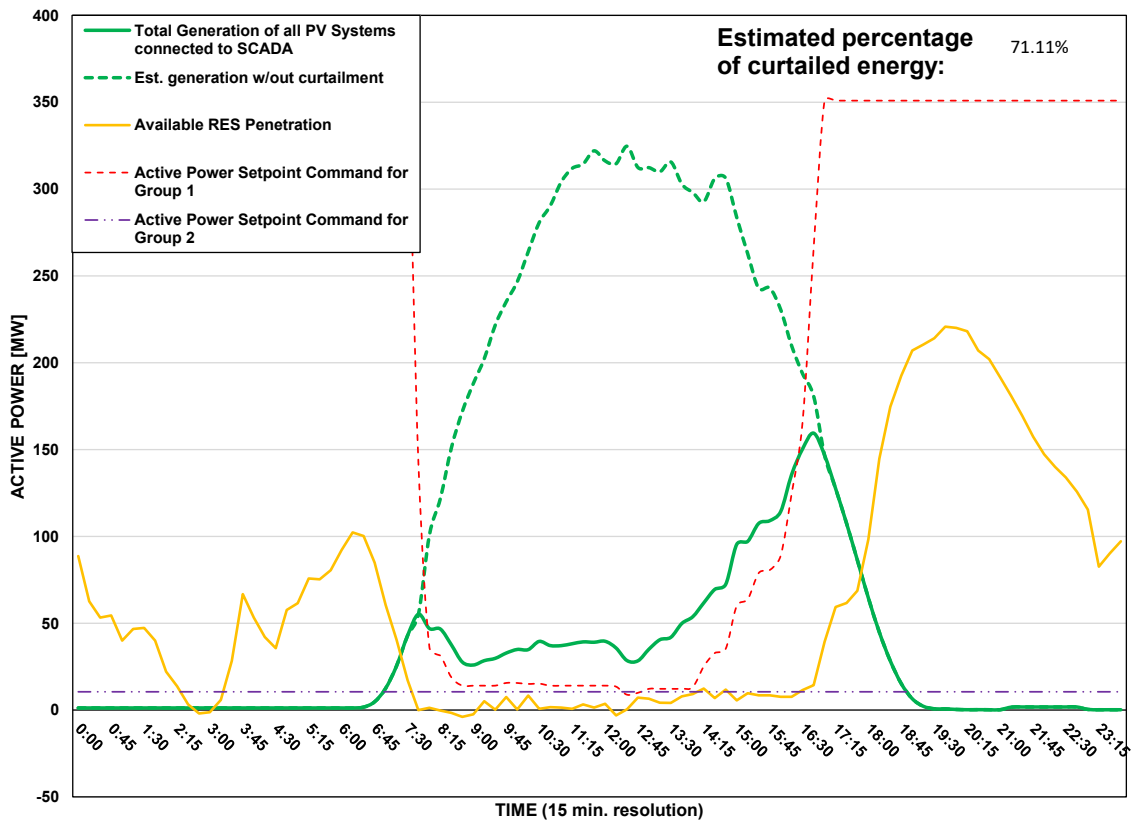

DISTRIBUTION SYSTEM OPERATOR SYSTEM OPERATION



Αρχή Ηλεκτρισμού Κύπρου
Διανομή

PV Generation Curtailment Report

Date of Curtailment:	31/08/2026
Start of Curtailment (G1 - non Priority)	9:45
End of Curtailment (G1 - non Priority)	15:00
Instruction from TSOC	YES
Reason of Curtailment:	RES-E Generation Restriction due to low loading of the electrical system
Total Estimated Energy of the day:	2396.8 MWh
Total Estimated Curtailed Energy:	495.8 MWh
Percentage of Curtailed Energy:	20.69%

Scada PVs Generation on 31/08/2026 (curtailment time: 09:45 - 15:00)

